



# Homestead High School

Summer Projects

4310 Homestead Road

Fort Wayne, IN 46814



## Construction Progress Update - 7.24.2020

### This Week

Continued Stud Wall Framing (CMT)  
 Continued MEP In Wall and Overhead Rough-Ins (CMT)  
 Began Server Room Stud Walls and Roof (CMT)  
 Completed Reception Counter and Existing Casework (Attendance Office)  
 Completed Install of VCT Flooring and Sealing (Boiler Room Expansion)  
 Received Final Inspection and Occupancy (CTE/PLTW)

Began In-Wall Blocking (CMT)  
 Completed Setting Jam Channels at Overhead Door (CMT)  
 Began Setting Moveable Temporary Fence (Phase 1)  
 Received Final Inspection and Occupancy (Attendance Office)  
 Received Final Inspection and Occupancy (Boiler Room Expansion)  
 Received Final Inspection and Occupancy (Locker Room Temporary Wall)

### Next Week

Complete Stud Wall Framing (CMT)  
 Complete MEP In-Wall Rough-Ins (CMT)  
 Begin Hanging Miscellaneous Drywall (CMT)  
 Begin RTU Replacement (CMT)  
 Begin Demolition of CMT for New Chiller (CMU)  
 Continue Setting Temporary Construction Fencing (Phase 1)

Continue MEP Overhead Rough-Ins (CMT)  
 Continue In-wall Blocking (CMT)  
 Begin Install of DensGlass and Liner Panel on Server Room (CMT)  
 Begin Generator Pad (CMT)  
 Begin Setting Door Frames in Offices (CMT)  
 Begin Sitework Demolition (Phase 1)


### Milestone Events

Begin Sitework Demolition (Phase 1) - 7.30.20  
 Set Door Frames (CMT) - 7.30.20

Receive In-wall Inspection (CMT) - 7.31.20  
 Begin Hanging Drywall (CMT) - 8.31.20


### Progress Photos

## CMT

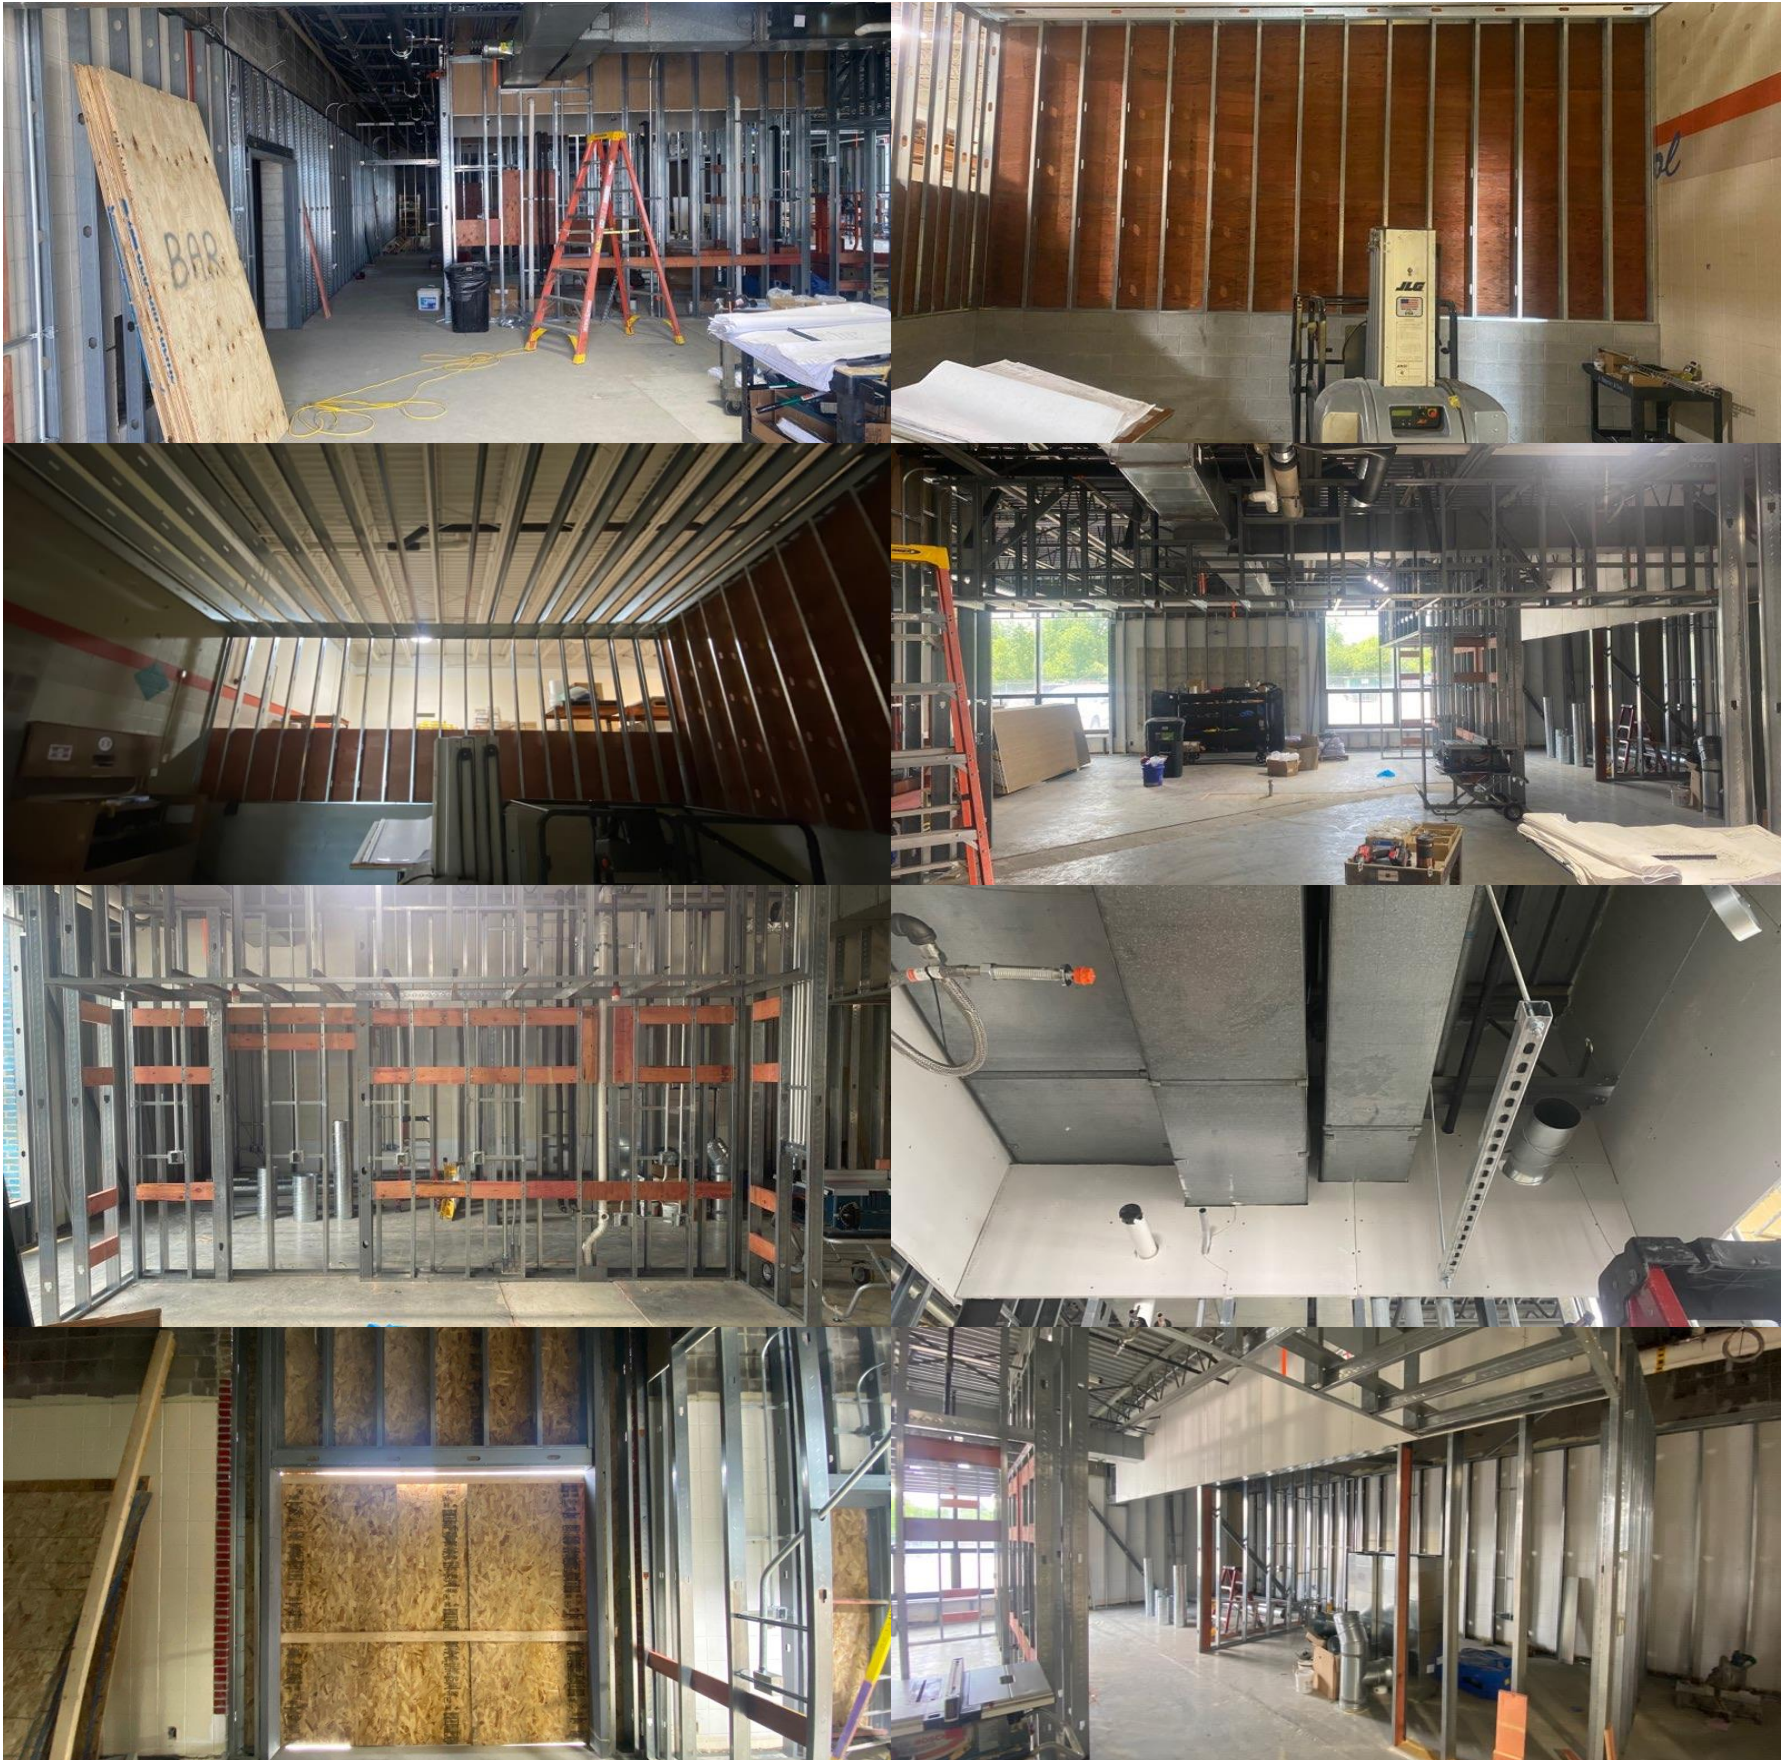



**ATTENDANCE OFFICE**

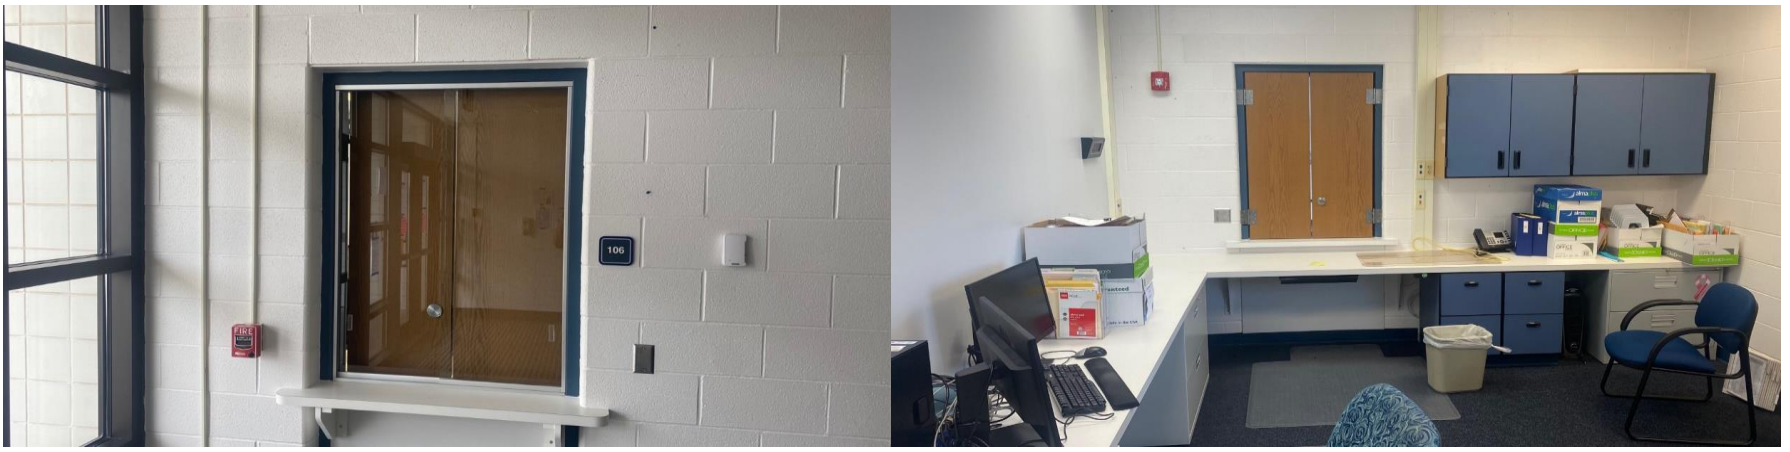

**BOILER ROOM EXPANSION**

