



# Homestead High School

Addition and Renovation

4310 Homestead Road

Fort Wayne, IN 46814



## Construction Progress Update - 10.9.2020

### This Week

Completed Install of Casework and Countertops (CMT)  
 Completed Final Coat of Paint (CMT)  
 Continued Server Room Connections (CMT)  
 Began Install of Kitchen Appliances (CMT)  
 Completed Detention Pond Concrete Chutes (Phase 1)  
 Began Underground Electrical in New Student Lot (Phase 1)

Completed MEP Overhead Rough-ins (CMT)  
 Completed Install of Carpet & Ceramic Tile (CMT)  
 Began Install of Open Office Furniture (CMT)  
 Continued Rough Grading of New Student Parking Lot and Detention Pond (Phase 1)  
 Continued Underground Storm Piping for New Visitor/Student Parking Lot (Phase 1)  
 Completed Softball Concession and Dugout Concrete Foundations (Phase 1)

### Next Week

Conduct Final Clean (CMT)  
 Complete Open Office Furniture Install (CMT)  
 Complete Install of Interior & Exterior Signage (CMT)  
 Begin Topsoil & Seeding of Detention Pond (Phase 1)  
 Begin Fine Grade & Stone of New Student Lot (Phase 1)  
 Begin Turn Down Walks at Perimeter of New Student Lot (Phase 1)

Complete Sealing of Exposed Concrete (CMT)  
 Complete Kitchen Appliances Install/Hook-Ups (CMT)  
 Begin Framing for Exterior Chiller Screen Wall (CMT)  
 Continue Underground Storm Piping for New Student Parking Lot (Phase 1)  
 Begin Install of Softball Field Subdrainage & Irrigation System (Phase 1)  
 Begin Preparation for New Main Entrance Drive (Phase 1)


### Milestone Events


Server Room Completion / Startup (CMT) - 10.9.20  
 Punchlist (CMT) - 10.15.20

Final Clean (CMT) - 10.12.20  
 Begin Sequence 3 for Main Entrance Drive (Phase 1) - 10.15.20

### Progress Photos

## CMT

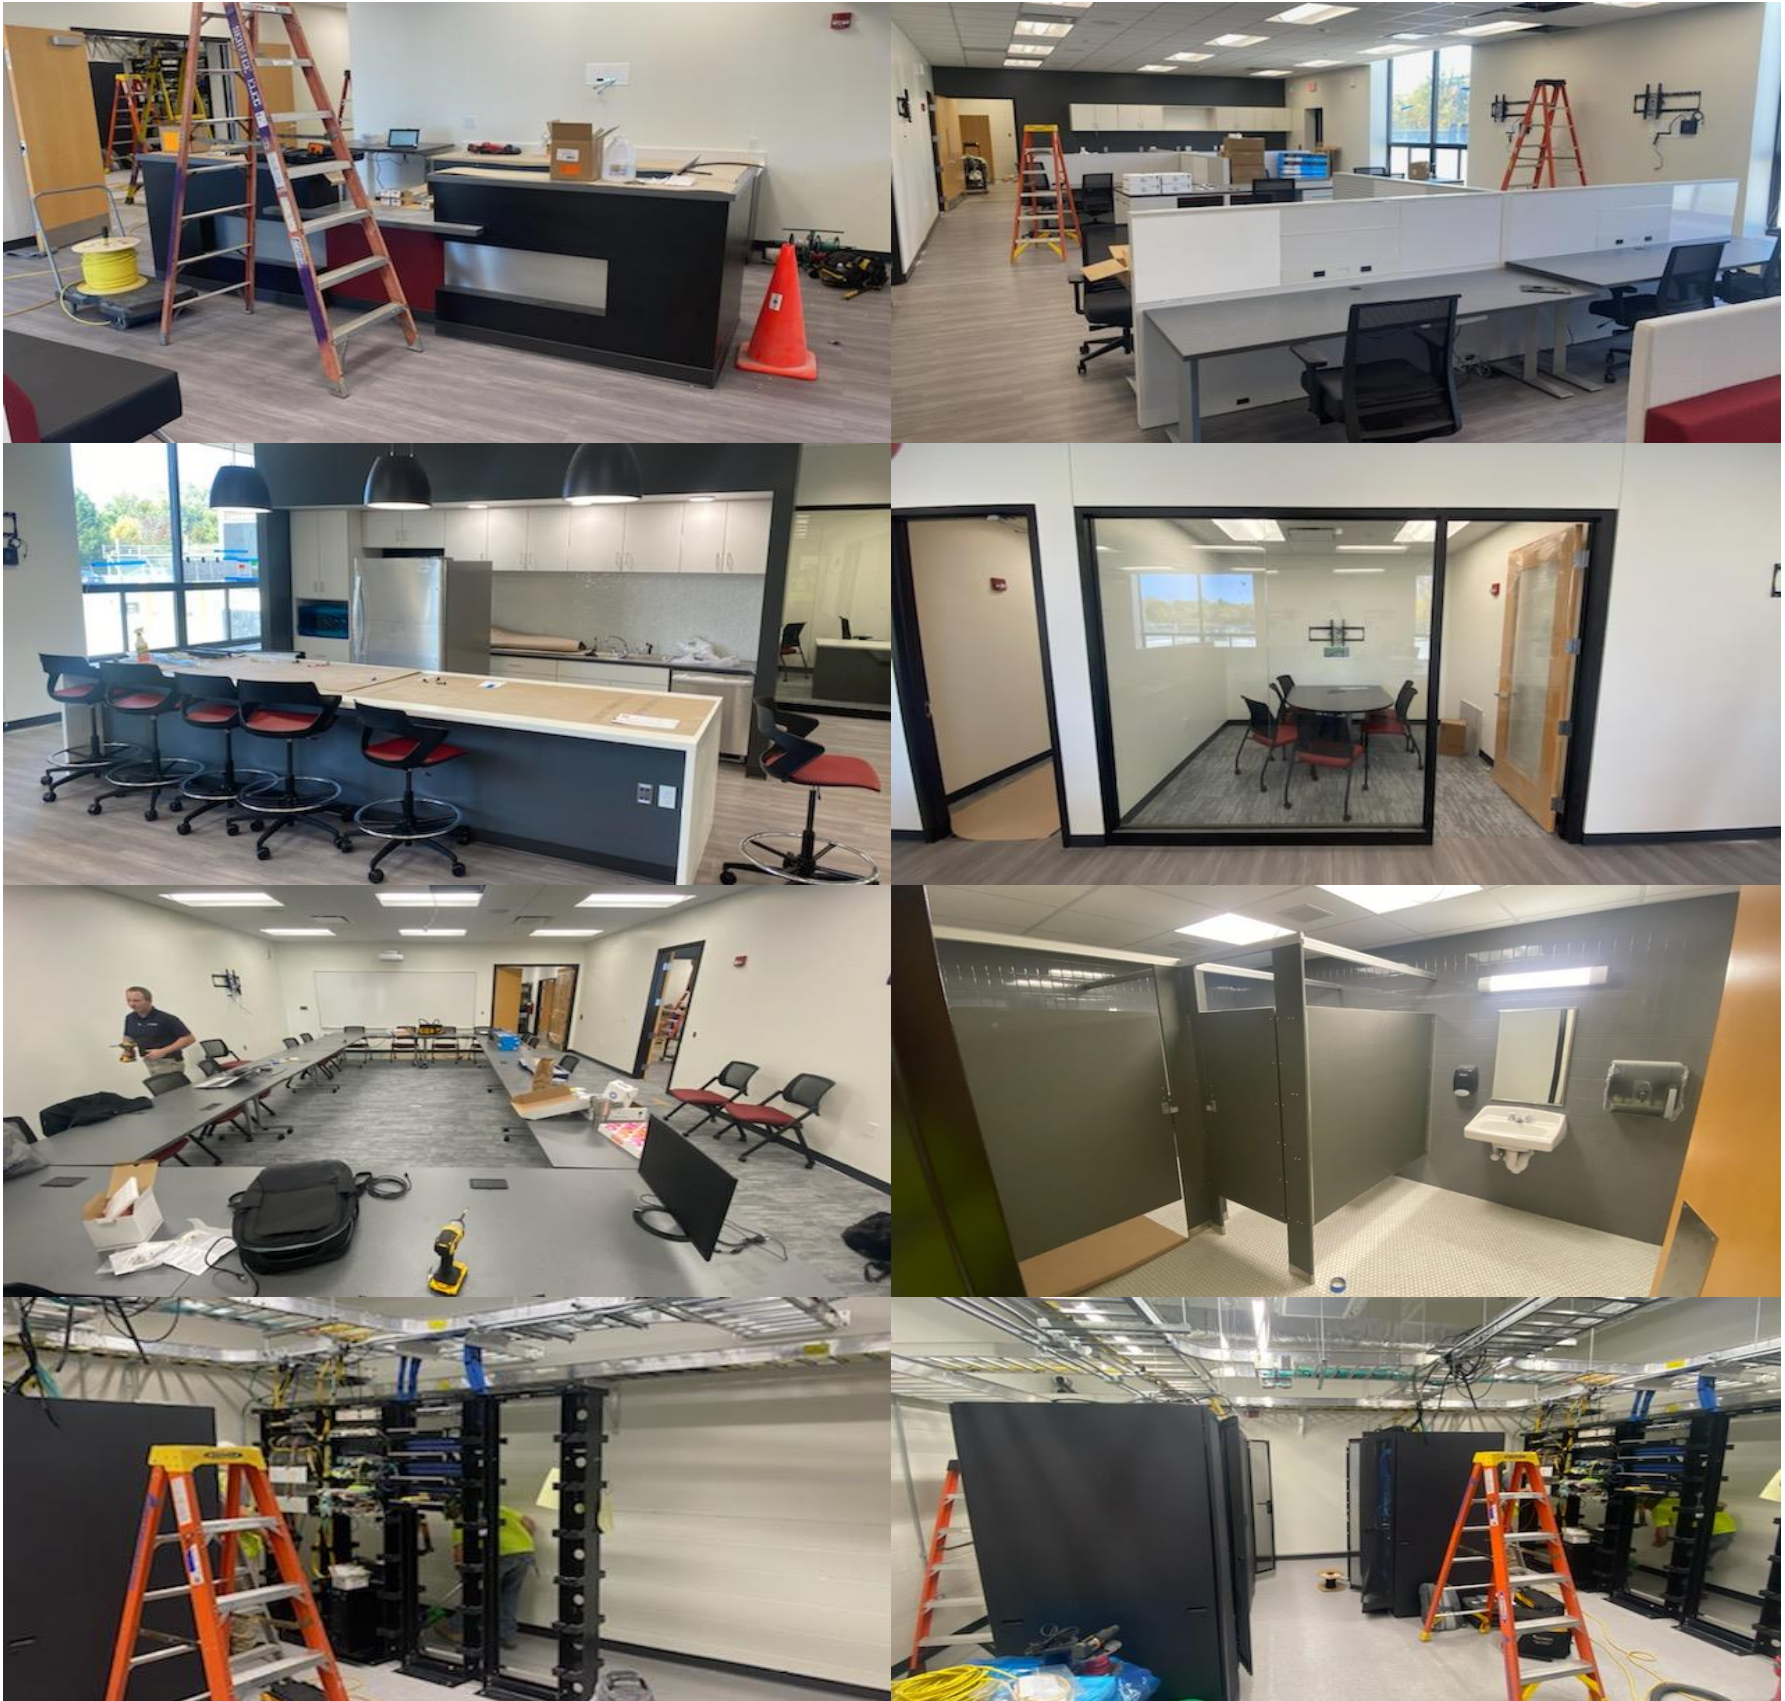

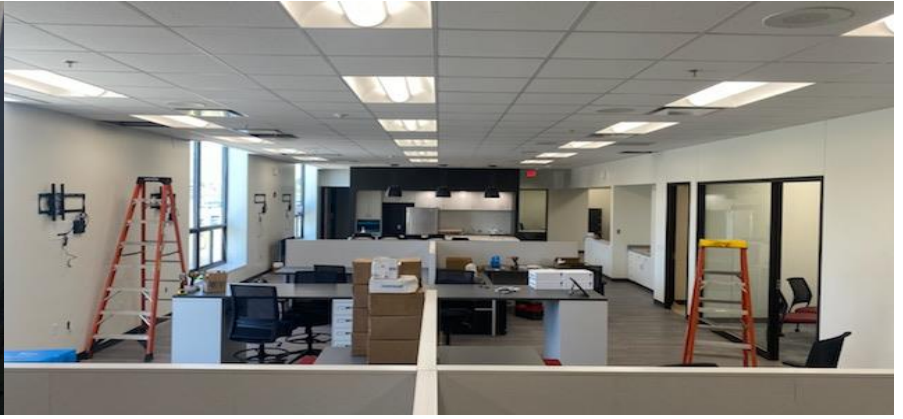

Phase 1

